

Ringwood Gateway

Contractor update

Dear community / visitors


Osborne is pleased to update you on our progress at the Ringwood Gateway project.



The brickwork, as detailed in the original design plans that were approved by the local councils, is now complete to all areas, including the glazed brick feature panels for the public toilets.



Felt and batten is almost complete to both sides of the pitch roof and internal partitions and walls are mostly constructed across both floors.

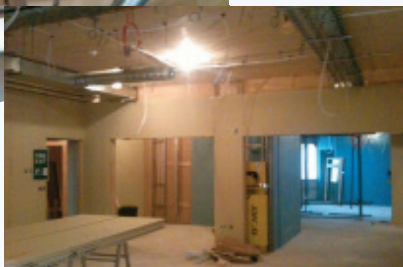

Mechanical and electrical first fix installations are almost complete including ductwork and associated units.



Site Contact: Lee Stoker
email: lee.stoker@osborne.co.uk

Works planned for the forthcoming month

- Installation of external doors and windows
- Slates to pitch roof
- Flat roof coverings
- Ceiling installations
- Internal doorsets

Scan your smart phone



ringwood.gov.uk/gateway

Summary
The project remains on programme.

Working together to save money
